Status Report

*This document contains all relevant important information regarding the project status as of **05.04.2026**.*

Management Summary

We've started working on the main part of the project being the web-editor. Unfortunately, we have been unable to finish the editor, therefore leaving a decent number of issues unfinished, settings us behind of schedule. Furthermore, we've added more issues, which are connecting the frontend with backend, which we've mostly finished for what's planned for the current sprint. Additionally, a few issues have been left incomplete due to being forgotten. Overall, we are slightly behind, however, we should still be able to finish the project with no big amount of stress.

1. Kanban Board

This is the final status of the Current iteration view in GitHub:

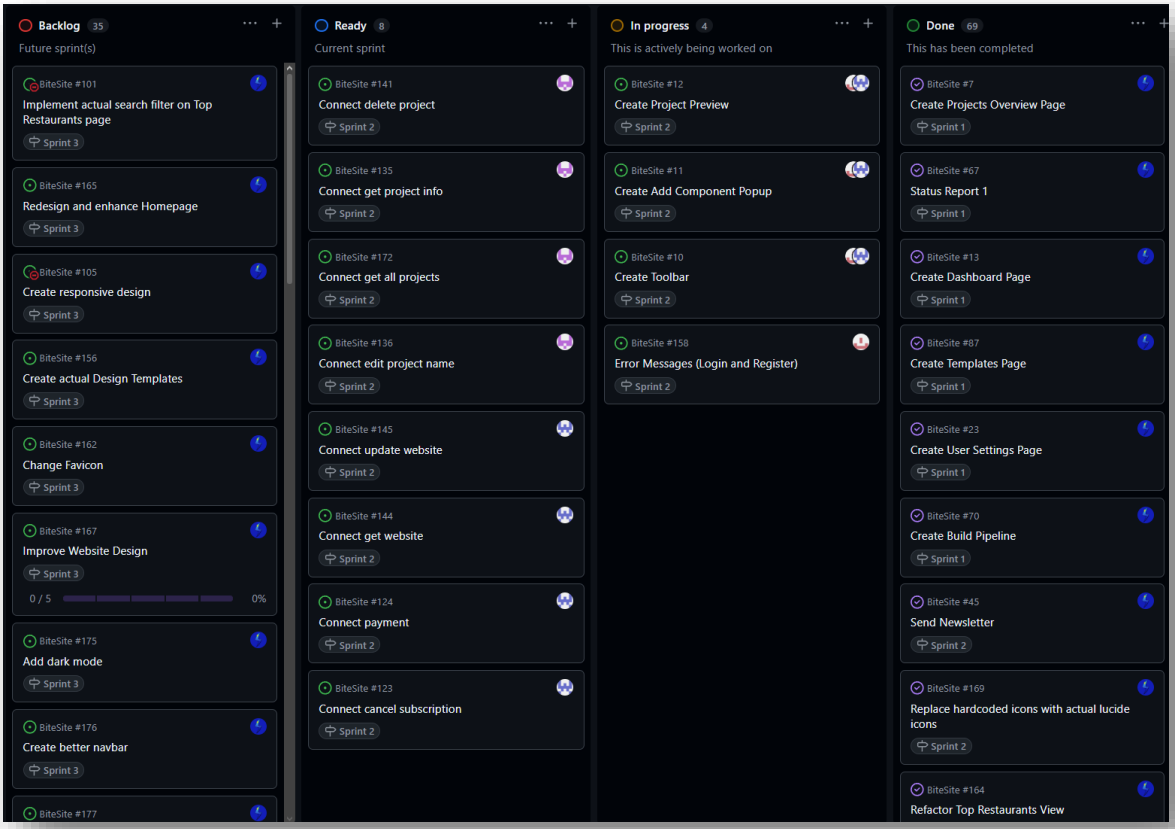

We were unable to finish the web-editor, because we've underestimated the difficulty of it. Therefore, we were unable to complete all issues related to the editor, settings us behind of schedule. More time needs to be invested in the following sprint to complete the editor, as we doubt it's a question of skill, more a question of time to figure it out.

2. Results

The web-editor has been started, though it's currently unfinished. We've added issues to connect all frontend and backend, which we've now completed for sprint 1 and sprint 2, except the ones related to the web-editor. The newsletter page has been set up, connected to the backend and successfully tested; however, it's currently being sent to junk mail only, which needs to be fixed. Furthermore, user accounts are now connected to the backend. Projects can now be created, published and unpublished, as well as a few more features to it. The overall design of the website has been made consistent, although design changes are expected to happen during the following sprint, as we're not fully satisfied with it.

3. Insights

As mentioned, we've underestimated the difficulty of the web-editor overall. Additionally, we noticed a few necessary features have been forgotten to be implemented in the frontend to begin with. We have fixed most of them, but we're certainly going to find more as we progress. Lastly, our server has been down due to private issues, however, that should be fixed very soon at the beginning of the following sprint and should not cause any issues.

4. Decisions

We've decided to move some issues, such as design-related issues (and due to delay the web-editor automatically too) to the last sprint. The editor has also been handed off from one group member to another due to lack of coding abilities including with help of AI tools. Furthermore, some issue assignments have been reassigned to other group members due to different skill levels. These issues are mostly related to connecting the frontend to the backend.

5. Risks

It turns out that despite having help such as AI tools, some of the group members are unable to fulfill their tasks due to lack of skills and must hand them off to the other group members, delaying us in our progress. We can overcome the risk of getting delayed even more by letting the other group members work overtime, which will probably be the case, so therefore the project should still be manageable on time. Otherwise, there should be no other risks preventing us from completing our project in time.

6. Conclusion

We are slightly behind schedule. More time will be needed to be invested in the project, especially in the web-editor, probably outside of school times too. However, the end goal of our project still seems very doable.

7. Forecast

Our highest priority is to get the editor and all its related issues done. We will then proceed with the issues assigned to the last sprint. This includes all reservations-related issues, reviews-related issues and polishing the project as finalization.

8. List of References

- ChatGPT and Codex for helping with writing code, debugging and refactoring.

9. Honesty Declaration

Gruppenarbeiten

Die Unterzeichnenden bestätigen, dass alle Gruppenmitglieder einen gleichwertigen Beitrag zur vorliegenden Arbeit geleistet haben. Wir sind damit einverstanden, dass alle die gleiche Note erhalten. Die Unterzeichnenden versichern, dass die vorliegende Arbeit selbständig und ohne Benutzung anderer als der in der Dokumentation angegebenen Quellen und Hilfsmittel angefertigt wurde. Die funktional oder inhaltlich den verzeichneten Quellen und Hilfsmitteln entnommenen Stellen sind als solche kenntlich gemacht. Diese Arbeit ist noch nicht veröffentlicht und noch keiner Prüfungsbehörde vorgelegt worden.

Wir nehmen zur Kenntnis, dass das Nichtdeklarieren von funktional oder inhaltlich von anderen Personen oder künstlicher Intelligenz übernommenen Ideen gegen das Gebot der Redlichkeit und gegen Autorenrechte verstösst, dass diese Bestimmungen missachtende Arbeiten als Plagiate gelten und dass entsprechende Vergehen dazu führen, dass die betroffene Arbeit mit 0 Punkten bewertet wird und weitere rechtliche Schritte eingeleitet werden.

Sursee, 05.03.26	
Sursee, 05.03.26	
Sursee, 05.03.26	
Sursee, 05.03.26	
